

Progress Status of Covering the Marine Soil of the Port of Fukushima Daiichi Nuclear Power Station

< Reference >

May 16, 2012

Tokyo Electric Power Company

[Unit 1-4]

March 14: Started working on the first covering layer

March 29: The first covering layer completed

April 5: Started working on the second covering layer




May 11: The second covering layer completed

[Unit 5-6]

May 16: Silt fence installation

May 17: Will start working on the first covering layer

End of June: The first covering layer will be completed

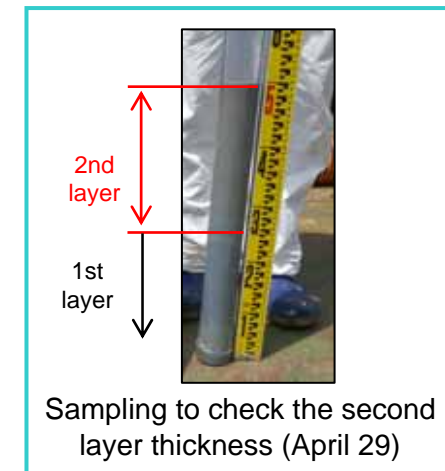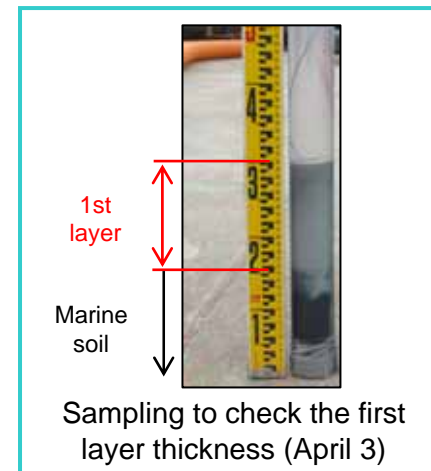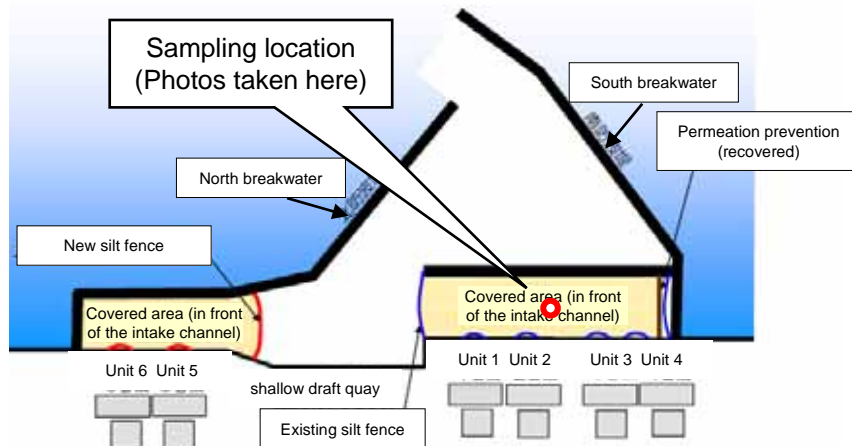

We have confirmed that the first layer is fully covering the seafloor surface.
We have also confirmed that the second layer is fully covering the first layer, and the specified thickness is maintained.
