
[m<sup>3</sup>/day]

## Changes in the amount of water transferred from groundwater drains to reactor and turbine buildings and in the amount of groundwater and rainwater flowing into the buildings

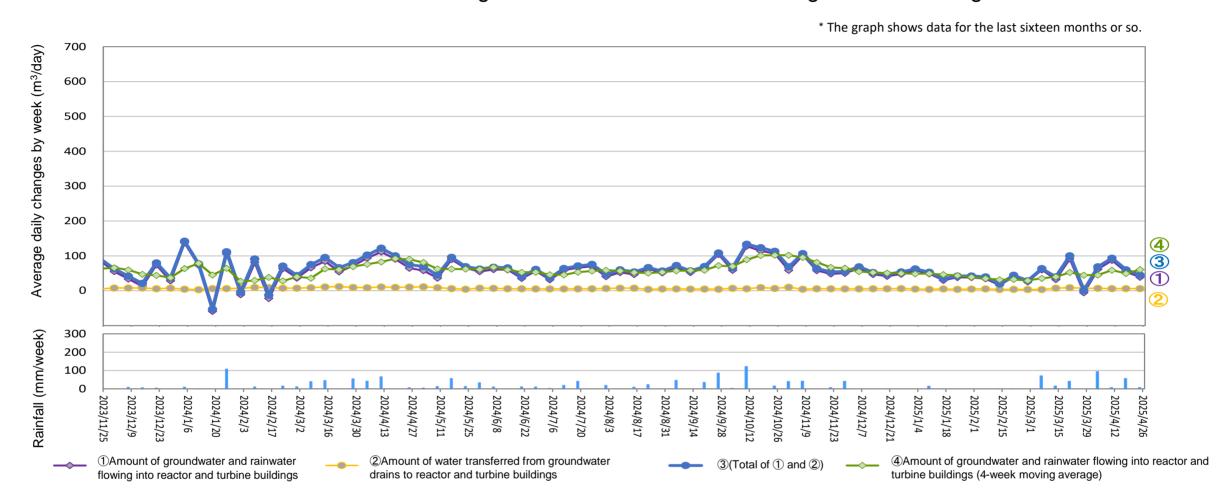

Amount of water transferred from groundwater drains to reactor and turbine buildings (From Apr 17, 2025 to Apr 23, 2025)

Date	Temporary storage tanks				
	А	В	С	Total (α)	
From Apri 17 to Apr 23	0	0	0	0	

	eference) improved			
(Re	(Reference)			
Between Units 1-2	Between Units 2-3	Between Units 3-4	Total (β)	Amount of water transferred to turbine buildings $[(\alpha)+(\beta)]$
6	0	0	6	6

①Amount of groundwater and rainwater flowing into reactor and turbine buildings: 39 m³/day, ②Amount of water transferred from groundwater drains to reactor and turbine buildings: 6 m³/day, ③(Total of ① and ②): 45 m³/day, Rainfall: 7.0 mm/week

There may be a difference between the sum of the individual data and the total value since the total value is the sum of the data with the first decimal place.

(Reference) ④ Amount of groundwater and rainwater flowing into reactor and turbine buildings (4-week moving average): 61 m³/day

<sup>\*</sup> Figures for ①, ③ and ④ have been calculated after elaborating some of cross sectional area of the process main building since April 4, 2024. Nevertheless, figures may be estimated to be a negative value since the calculation still contains uncertainty.

(Reference) Changes in the amount of water transferred from groundwater drains to reactor and turbine buildings and in the amount of groundwater and rainwater flowing into the buildings from the start of measurement

