
Mistaken Transport of Accumulated Water to the Incineration Workshop Building at <Reference> the Central Radioactive Waste Treatment Facility of the Fukushima Daiichi Nuclear **Power Station**

Turbine

April 14, 2014 **TEPCO**

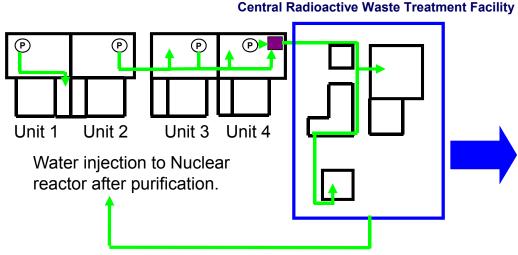

Accumulated water of the Processing main building was mistakenly transferred to the Incinerator work building, which resulted in flowing out to the first basement.

- There are no points which pass through to outside the building on the layout.
- There is no significant change shown in the analysis result of subdrain water around the Incinerator work building
- The water level of subdrain water is high enough against the water level of the Incinerator work building.
- There is no change in the water levels of either the incinerator building or the work building.
- ⇒ By which, it is estimated that there is no leakage occurred outside the Incinerator work building.

Transfer line used for accumulated water transportation on a regular basis.

Transfer line with pump turned on, which is not in use for accumulated water transportation on a regular basis.

