

Fukushima Daiichi Nuclear Power Station Completion of the Discharge from Measurement/Confirmation Facility Tank Group A (Third Discharge)

< Reference document >
November 20, 2023
Tokyo Electric Power Company Holdings, Inc.
Fukushima Daiichi Decontamination and
Decommissioning Engineering Company

- The discharge of ALPS treated water from measurement/confirmation facility tank group A began on November 2 (approximately 7,800m³), planning to take approximately 17 days.
- Samples have been taken from the seawater pipe every day to measure tritium concentrations in order to confirm that tritium is being suitably diluted during the discharge period. As a result, we have been able to confirm that the analysis values are approximately equal to calculated concentrations, and below 1,500Bq/liter.
- Seawater samples have also been taken every day, and the detection limit has been raised to approximately 10Bq/liter in order to quickly obtain tritium concentration measurement results. As a result, we have confirmed that the analysis values are below both the discharge suspension level (700Bq/liter) and the investigation level (350Bq/liter).

< Announced by November 19 >

- Since the commencement of discharge on November 2, the amount of ALPS treated water being discharged has remained constant at approximately 460m³/day, and daily quick analysis results of tritium concentrations in the seawater have confirmed that the ALPS treated water is being discharged safely as planned.
- The transfer of ALPS treated water from measurement/confirmation facility tank group A was completed at 10:18 AM on November 19. On November 20, the flush out of the water remaining in the ALPS treated water transfer line was completed at 0:01 PM and the completion of this task marked the end of the third discharge of ALPS treated water into the sea. (Total amount of water discharged: approx. 7,753 m³, Total amount of tritium discharged: approx. 1.0 trillion Bq)
- After draining the water in the upper-stream storage, we will conduct the inspections regarding facilities and its operations such as follow-up observation of waterproof coating condition inside the upper-stream storage which was previously observed.
- Furthermore, we will conduct a comprehensive review of the three discharges carried out to date, and will announce the results as soon as it is summarized.
- Going forward, we will remain vigilant to ensure that there are no unintentional discharges of ALPS treated water into the sea.

[Reference] Manual shutdown by operators (in response to sea area monitoring)

Partially edited excerpt from "Attachment 1: Information about the Discharge of Multi-nuclide Removal Equipment Treated Water into the Sea" (published on August 22, 2023)



- Seawater tritium analysis is implemented once a week at all points on Figures 1 and 2 below, with the detection limit set to 0.1-0.4Bq/liter.
- In addition, quick tritium measurements with the detection limit set to 10Bq/liter will be implemented at the locations outlined in the red frames in Figures 1 and 2 below. In the case "discharge suspension level" indicators are exceeded, the discharge into the sea will be suspended.
- After the commencement of the discharge, in light of the monitoring frequency outlined by the various organizations within the Comprehensive Monitoring Plan, frequency of quick tritium measurements specifically near the discharge outlets shown in Figure 1 will be increased from once a week to everyday for the time being.

Figure 1. Sampling locations within a 3km radius of the power station (in the vicinity of the discharge outlet)


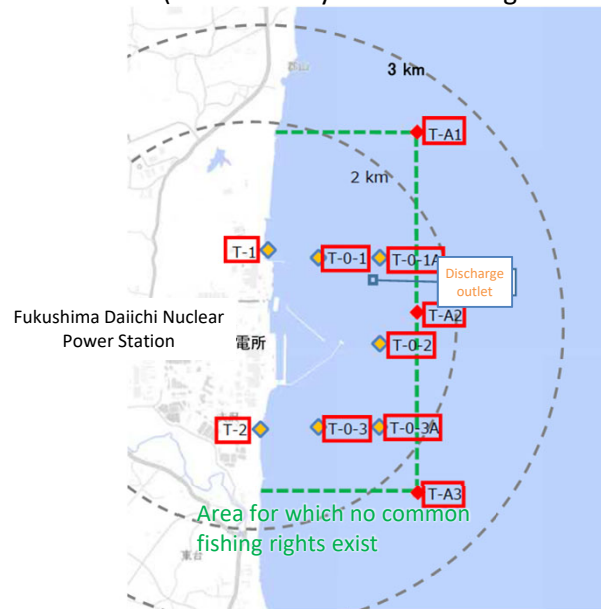


Figure 2. Sampling locations within a 10km square in front of the power station



[Red Box] : Monitoring locations for quick tritium measurements (10 locations)
Indicator (discharge suspension level): 700Bq/liter
 Analysis frequency: once a week → Every day for the time being

[Red Box] : Monitoring locations for quick tritium measurements (4 locations)
Indicator (discharge suspension level): 30Bq/liter
 Analysis frequency: Once a week (T-D5),
 Once a month (T-S3, T-S4, T-S8)

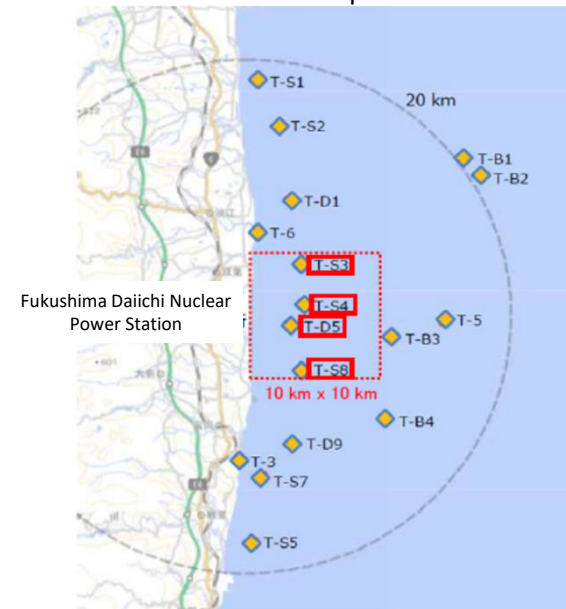

[Reference] FY2023 Discharge Plan

- Currently, we are performing facility inspection after the second discharge (tank group C). If no abnormalities are found in the inspection, we will transfer ALPS treated water to transfer pipe on October 30 and will commence the 1st Stage of the third discharge on October 31. The 2nd Stage, which marks the beginning of the third discharge (tank group A) of ALPS treated water into the sea, will start on November 2.

1 st discharge	Measurement/confirmation facility (K4 area) Group B:	Approx. 7,800m ³	Secondary treatment: No Tritium concentration: 140,000Bq/liter Total amount of tritium: 1.1 trillion Bq	Completed
2 nd discharge	Measurement/confirmation facility (K4 area) Group C:	Approx. 7,800m ³	Secondary treatment: No Tritium concentration: 140,000Bq/liter Total amount of tritium: 1.1 trillion Bq	Completed
3 rd discharge	Measurement/confirmation facility (K4 area) Group A:	Approx. 7,800m ³	Secondary treatment: No Tritium concentration: 130,000Bq/liter Total amount of tritium: 1.0 trillion Bq	Details on the next page
4 th discharge	K4 area Group E (Transferred to Measurement/confirmation facility group B ※ ²): K3 area Group A (Transferred to Measurement/confirmation facility group B ※ ²):	Approx. 4,500m ³ Approx. 3,300m ³	Secondary treatment: No Tritium concentration: 170,000~210,000Bq/liter ※ ¹ Total amount of tritium: 1.4 trillion Bq ※ ¹	

➡ Total amount of tritium discharged during FY2023: Approx. **5 trillion Bq**

※¹ Average value of the tank group that was assessed taking into account the radioactive decay until July 1, 2023

※² To be transferred to K4 area tank group B that will be empty after the 1st discharge is completed

[Reference] Outline of third discharge for Group K4-A

Outline of discharge for group K4-A			
Attributes of the treated water	Concentration of the 29 types of radionuclides (excluding tritium) in scope of measurement/evaluation	Within regulatory requirements (sum of the ratios of legally required concentrations of radioactive substances is less than 1) (sum of the ratios of concentration: 0.25*) <small>(details on p1 of the link)</small>	
	Tritium concentration	130,000Bq/liter <small>(details on p2 of the link)</small>	
	Concentration of the 39 significant types of radionuclides measured voluntarily	No significant radionuclides identified <small>(details on p3 of the link)</small>	
	Status of water quality assessment	Within government and prefectural requirements <small>(details on p4 of the link)</small>	
	Water temperature	Same as outdoor temperature. After diluted to 740 times, same as sea water temperature (not the same as plant's thermal discharge)	
Expected volume of treated water discharge	Approximately 7,800m ³		
Treated water flow rate	Approximately 460m ³ /day (set not to exceed designed maximum on 500m ³ /day)		
Dilution sea water flow rate	Approximately 340,000m ³ /day (same speed as walking in the tunnel [approximated 1m/second])		
Concentration of tritium after dilution	Approximated 180Bq/liter		
Term of discharge	Approximately 17 days		

※ Comparison of concentrations before/after sea water dilution

	Before dilution	After dilution (740 times)
29 types	0.25	0.00034
Tritium	2.17	0.0029

0.0032 (1/310 of government requirements)
