

- The 6th (24th overall) discharge of ALPS treated water in FY2026 began at 11:21 a.m. on October 5.
- In order to ensure that the ALPS treated water (tritium) is properly diluted every day during the discharge period, we have analyzed the tritium concentration in the water after dilution with seawater and confirmed that the analysis values are approximately equal to calculated concentrations, and below 1,500 Bq/liter.
- During the discharge period, seawater samples have also been taken from 10 locations within 3 km of the power station and 4 locations within 10 km square in front of the power station, and the detection limit has been raised to approximately 10 Bq/liter in order to quickly obtain tritium concentration measurement results. As a result, we have confirmed that the analysis values are below both the discharge suspension level (700 Bq/liter^{*1} or 30 Bq/liter^{*2}) and the investigation level (350 Bq/liter^{*1} or 20 Bq/liter^{*2}).

*1 10 locations within 3 km of the power station *2 4 locations within 10 km square in front of the power station

< Announced by October 5, 2026 >

- During the 6th (24th overall) discharge of ALPS treated water in FY2026, the amount of the ALPS treated water being discharged remained constant at approximately 460 m³/day, and daily quick analysis results of tritium concentrations in seawater have confirmed that the ALPS treated water is being discharged safely as planned.
- We completed the discharge of the ALPS treated water from the measurement/confirmation facility tank group A at 3:22 p.m. on October 22. The flush out of the water remaining in the ALPS treated water transfer line (ALPS treated water) was completed at 12:09 p.m. on October 23, and the completion of this task marked the end of the 6th (24th overall) discharge of ALPS treated water in FY2026. (Total amount of water discharged: approx. 7,852 m³, Total amount of tritium discharged: Approx. 1.2 TBq)
- A comprehensive inspection (full internal inspection) of Group A Measurement/Confirmation Tanks will commence on October 23.
- For the facilities associated with the ocean discharge, we will continue our efforts for the early detection of abnormalities through planned inspections. If paint cracking, blistering, corrosion, or other issues are identified during inspections, we will carry out appropriate repairs as we have done to date and work to maintain the long-term integrity of the facilities.

[Reference] FY2026 Facility inspections overview



- Regular inspections are planned for FY2026 as shown in the table below.

Facility	Primary inspection details	Inspection status
Measurement/ confirmation facilities	Measurement/confirmation tank group A: Full internal inspections	Approximately from October 2026 to May 2027
	Circulation pumps: Bearing lubrication oil replacement	Approximately September to November 2026
	Agitators: Insulation resistance measurement	Approximately from October※ ¹ 2026 to May 2027
	Miscellaneous: Strainer cleaning, etc.	Approximately August※ ¹ 2026 to May 2027
Transfer facilities	ALPS treated water transfer pumps: Disassembly inspection	Approximately November 2026 to February 2027
	Emergency isolation valve-1: Disassembly inspection	Approximately November 2026 to February 2027
	Emergency isolation valve-2: External inspection	Approximately January to February 2027
	Miscellaneous: Strainer cleaning, etc.	Approximately August※ ¹ 2026 to May 2027
Dilution facilities	Seawater transfer pump system A: Gland packing replacement	Approximately November 2026 to February 2027
	Seawater transfer pump system B: Disassembly inspection	Approximately November 2026 to February 2027
	Seawater transfer pump system C: Gland packing replacement	Approximately November 2026 to February 2027
	Sea water transfer pipes/seawater pipe header: Internal inspection	Approximately November 2026 to February 2027
	Discharge vertical shaft (upper-stream storage): Internal inspection	Approximately November 2026 to February 2027
Discharge facilities	Discharge vertical shaft (down-stream storage), discharge tunnel: Internal inspection	Approximately December 2026 to February 2027
Seawater intake facilities	Partitioning weirs: External inspection	Approximately December 2026 to February 2027
	Intake channel system B: Cleaning, Internal inspection, repair	Approximately November 2026 to February 2027

※¹: Implemented during the equipment outage period of each system.

[Reference] FY2026 ALPS treated water discharge plan and actual (1/2)

- The FY2026 ALPS treated water discharge plan is as follows. There will be eight discharges during the year with an annual discharge of approximately 62,400 m³. The annual tritium discharge volume will be approximately 11 TBq. In addition, there may be slight differences between the planned and actual annual tritium discharge amounts due to factors such as differences in the analytical values at the source tank group and the measurement/confirmation tank group.

Underlined figures indicate actual values.

Management number※ ¹	Transfer source tank※ ²	Amount of water to be transferred ※ ³	Discharge period (Discharge volume)
26-1-19	H2 area Group J (Transferred to Measurement/Confirmation facility Group A) : <u>Approx. 7,390 m³</u> H1 East area Group C (Transferred to Measurement/Confirmation facility Group A) : <u>Approx. 390 m³</u>	Secondary treatment: None Sum of the ratios to regulatory concentrations: <u>0.31</u> Tritium concentration: <u>240,000 Bq/L</u> Total amount of tritium : <u>1.9 TBq</u>	Apr. 2-20 (<u>7,865 m³</u>)
26-2-20	H1 East area Group C (Transferred to Measurement/Confirmation facility Group B) : <u>Approx. 7,780 m³</u>	Secondary treatment: None Sum of the ratios to regulatory concentrations: <u>0.45</u> Tritium concentration: <u>170,000 Bq/L</u> Total amount of tritium : <u>1.3 TBq</u>	Jun. 1-20 (<u>7,927 m³</u>)
26-3-21	H1 East area Group C (Transferred to Measurement/Confirmation facility Group A) : <u>Approx. 3,580 m³</u> H1 East area Groups A/B (Transferred to Measurement/Confirmation facility Group A) : <u>Approx. 4,200 m³</u>	Secondary treatment: None Sum of the ratios to regulatory concentrations: <u>0.48</u> Tritium concentration: <u>170,000 Bq/L</u> Total amount of tritium : <u>1.3 TBq</u>	Jul 6-24 (<u>7,894 m³</u>)
26-4-22	H1 East area Groups A/B (Transferred to Measurement/Confirmation facility Group C) : <u>Approx. 7,770 m³</u>	Secondary treatment: None Sum of the ratios to regulatory concentrations: <u>0.61</u> Tritium concentration: <u>170,000 Bq/L</u> Total amount of tritium : <u>1.3 TBq</u>	Jul. 30 - Aug. 17 (<u>7,888 m³</u>)

Continues on next slide

※¹ The management number is made up of the fiscal year, followed by the discharge number for that fiscal year, and the total number of discharges to date.
For example, "26-1-19" indicates that the data is for the first discharge of FY2026, which is the nineteenth discharge to date.

[Reference] FY2026 ALPS treated water discharge plan and actual (2/2)



Continued from previous slide

Underlined figures indicate actual values.

Management number ※1	Transfer source tank ※2	Amount of water to be transferred ※3	Discharge period (Discharge volume)
26-5-23	H1 East area Groups A/B H2 area Group B	(Transferred to Measurement/Confirmation facility Group B) : <u>Approx. 4,570 m³</u> (Transferred to Measurement/Confirmation facility Group B) : <u>Approx. 3,200 m³</u>	Secondary treatment: None Sum of the ratios to regulatory concentrations: <u>0.52</u> Tritium concentration: <u>160,000 Bq/L</u> Total amount of tritium : <u>1.3 TBq</u> Aug. 31 - Sep. 18 (7,863 m³)
26-6-24	H2 area Group B K1 area Groups C/D	(Transferred to Measurement/Confirmation facility Group A) : <u>Approx. 5,890 m³</u> (Transferred to Measurement/Confirmation facility Group A) : <u>Approx. 1,880 m³</u>	Secondary treatment: None Sum of the ratios to regulatory concentrations: <u>0.30</u> Tritium concentration: <u>150,000 Bq/L</u> Total amount of tritium : <u>1.2 TBq</u> Oct. 5 - 23 (7,852 m³)
26-7-25	K1 area Groups C/D	(Transferred to Measurement/Confirmation facility Group C) : <u>Approx. 7,770 m³</u>	Secondary treatment: None Sum of the ratios to regulatory concentrations: <u>0.14</u> Tritium concentration: <u>180,000 Bq/L</u> Total amount of tritium : 1.4 TBq Discharge Start Timing: Scheduled for discharge starting October 26 (7,800 m³)
Inspection suspension (including full inspections of measurement/confirmation facility Group A)			
26-8-26	K1 area Groups C/D G4 South area Group C	(Transferred to Measurement/Confirmation facility Group B) : <u>Approx. 1,540 m³</u> (Transferred to Measurement/Confirmation facility Group B) : <u>Approx. 5,900 m³</u>	Secondary treatment: None Sum of the ratios to regulatory concentrations: 0.35 - 0.50 ※4 Tritium concentration: 190,000 Bq/L ※5 Total amount of tritium : 1.5 TBq Discharge Start Timing: February - March (7,800 m³)

➡ Total amount of tritium to be discharged during FY2026 : Approx. **11 T** Bq

※1 The management number is made up of the fiscal year, followed by the discharge number for that fiscal year, and the total number of discharges to date.

For example, "26-1-19" indicates that the data is for the first discharge of FY2026, which is the nineteenth discharge to date.

※2 The tank order from which water will be transferred will not be impacted by increases/decreases in the transfer volume (factual measurements). But order of discharge may be moved forward or backward.

※3 The underlined sections indicate actual values.

※4 Conservative values calculated from the analytical values of the seven major nuclides (Cs-134, Cs-137, Sr-90, I-129, Co-60, Sb-125, Ru-106) measured after ALPS treatment and storage in tanks, plus the maximum value of C-14 (0.11) or analytical value and an estimate of the total of other nuclides at 0.3. For H1 East-A, B, C and H2-B, the notification concentration ratio calculated from the analytical values of the seven major nuclides is added to the maximum value of C-14 (0.11) or analytical value, and the analytical values of other nuclides (values obtained by analyzing samples obtained by mixing water samples taken from each tank in each tank group).

※5 Average value of the tank group that was assessed taking into account the radioactive decay until April 1, 2026

[Reference] Measurement monitoring plan for obtaining quick results

TEPCO

- Since the commencement of ALPS-treated water discharge into the sea in August 2023, TEPCO has engaged in monitoring to obtain quick measurements of the concentration of tritium in seawater at 14 locations shown in the diagrams below (Upper detection limit: Approximately 10Bq/liter). The discharge is immediately suspended if any of the values exceed the discharge suspension level (noted in the diagrams)

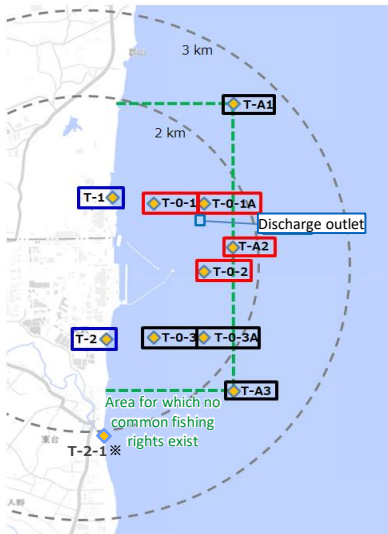


Figure 1: Specimen sampling locations within 3km of the power station (near the discharge outlet)

Red box, Blue box, Black box : Monitoring points used to obtain quick results (10 locations)
Indicator (Discharge suspension level) 700Bq/liter

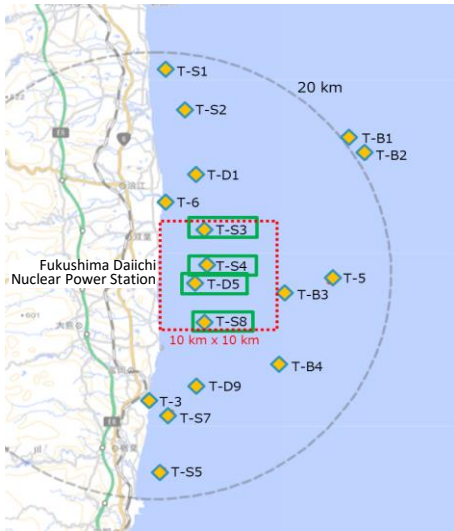


Figure 2: Specimen sampling locations within 10km square in front of the power station

Green box : Monitoring points used to obtain quick results (4 locations)
Indicator (Discharge suspension level) 30Bq/liter

	【Fig.1】 Within a 3km of the power station (near the discharge outlet)		【Fig. 2】 Four locations within a 10km square in front of the power station
	Four locations in the vicinity of the discharge outlet	Other six locations	
During the discharge period and for one week after the completion of discharge	Daily※1	Twice a week※2	T-D5: Once a week T-S3,T-S4,T-S8: Once a month
During the discharge suspension period (Excluding the week following the completion of discharge)	Once a week※2	Once a month※2	

※1 If bad weather during the discharge period prevents measurements from being taken for two consecutive days, on the following day (third day) if it is again expected that measurements cannot be taken, measured results will be quickly obtained from T-1 and T-2.

※2 We have engaged in monitoring daily since the commencement of discharge in August 2023, but the monitoring plan was changed on December 26, 2023 in light of actual measurements taken during discharge (Announced on December 25, 2023)
