

# Fukushima Daiichi NPS : Starting of dismantling flange type tanks at H2 area (For replacing to welded type tanks)

<Reference>

MAY 27,2015

Tokyo Electric Power Company

H2 area tanks (H2-C5) dismantling operation has begun today.


<Outline>

■ Date

May 27,2015 (Wed)

■ Operation detail (9:20~14:30)

- Removal of top board
- Installation of bottom-remained-water transport equipment
- Set up temporary top board

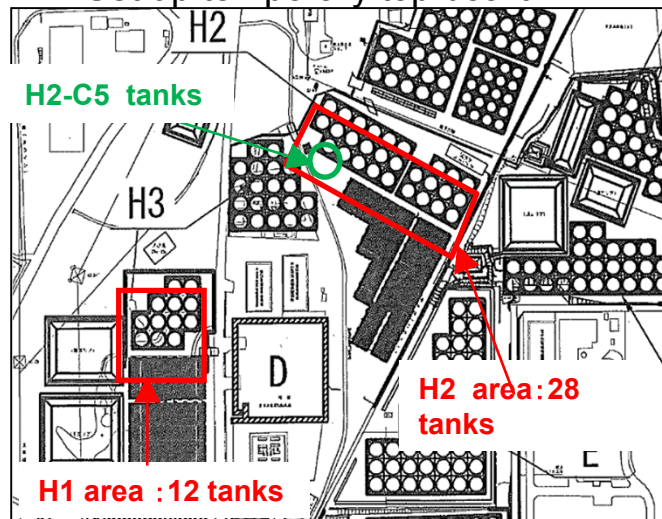

Removal of top board↑

**Opening top board**

Photo : Tokyo Electric Power Company  
Date: May 27,2015

←Setting up temporary top board

	2015						2016				
	5	6	7	8	9	10	11	12	1	2	3
H1 area flange type tank: 12 tanks		■									
H2 area flange type tank: 28 tanks	▽ 5/27	■									

\* The schedule is subject to change by such as bad weather

**Dismantling operation area**

**Dismantling operation process**
